





Current

go with the flow

what is current?

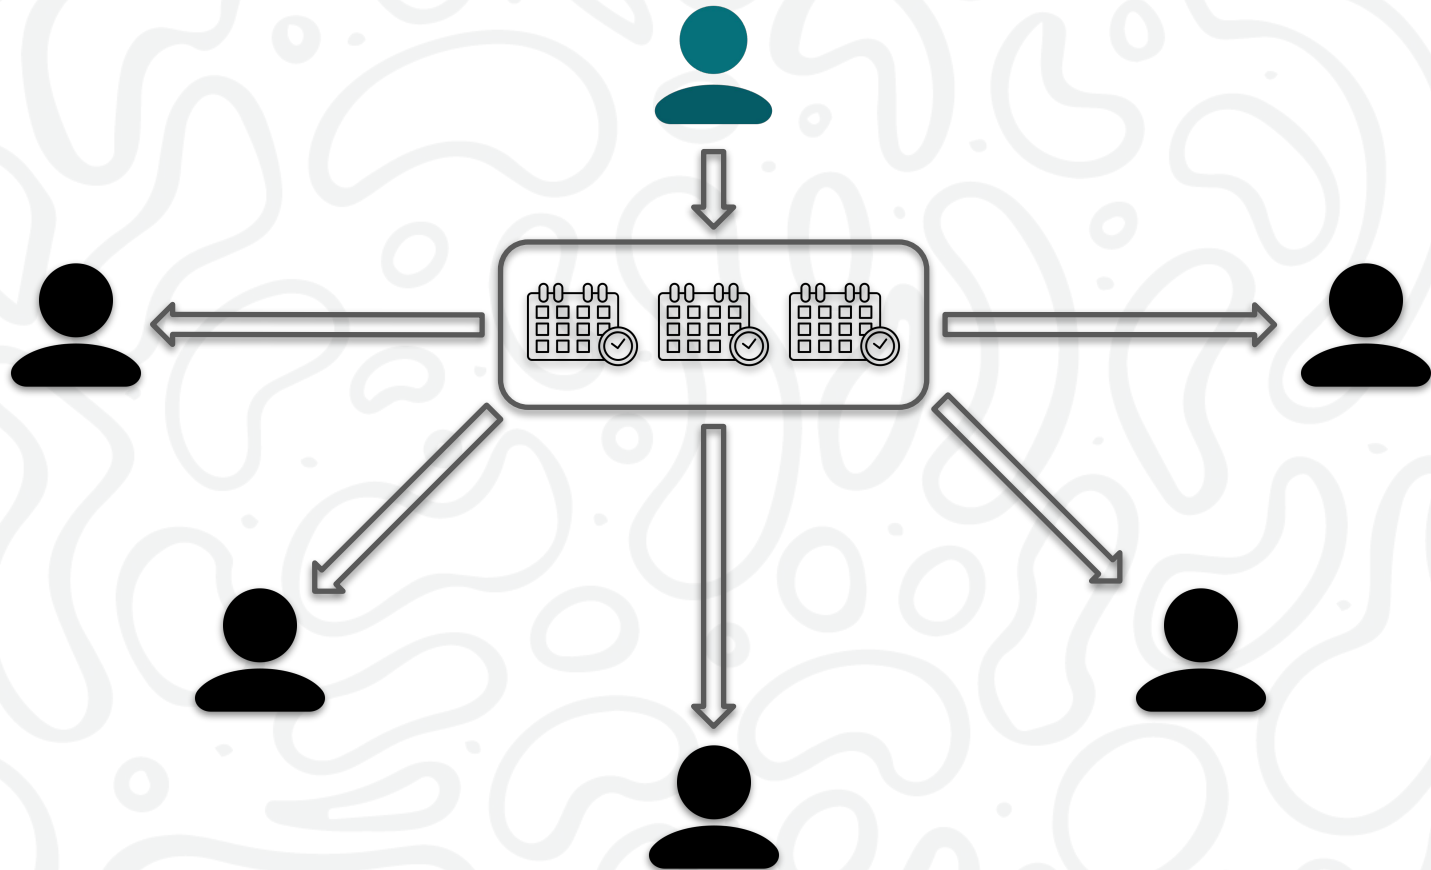

see it for yourselves!

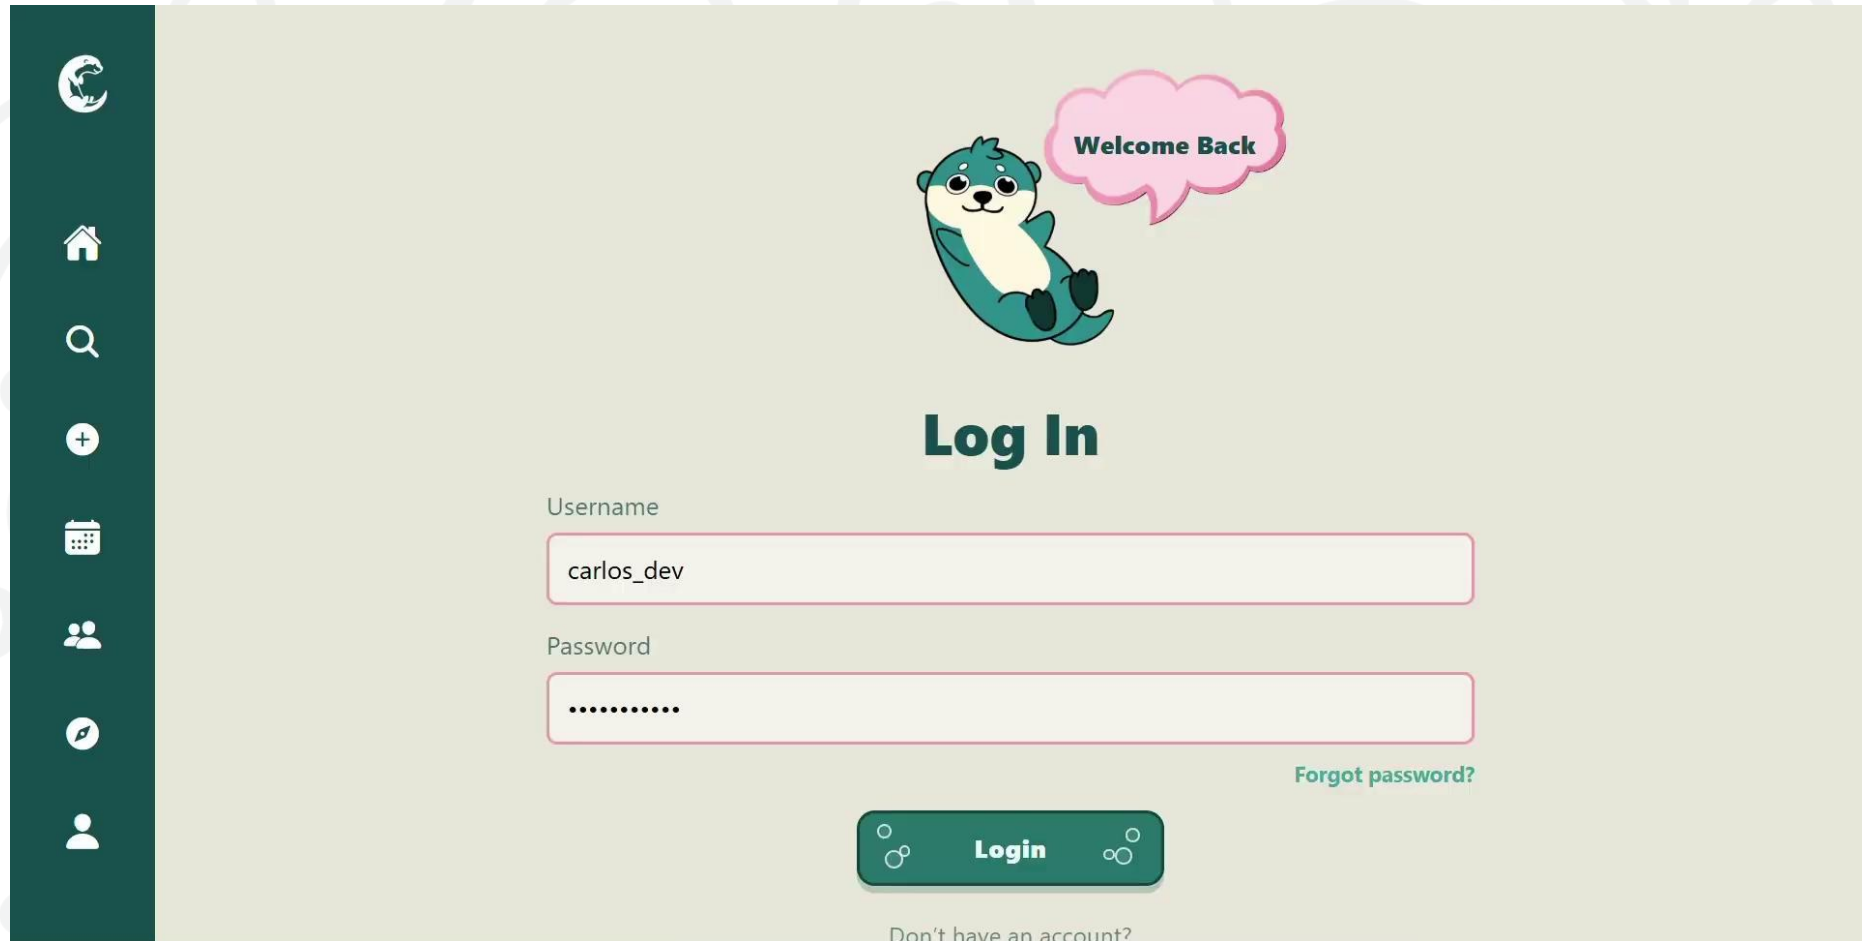

The screenshot shows a login interface. On the left is a dark green sidebar with icons for home, search, add, calendar, people, location, and profile. The main area has a light beige background. At the top center is a cartoon animal (a blue and white creature) with a pink speech bubble saying "Welcome Back". Below this is the "Log In" heading. There are two input fields: "Username" with the text "carlos_dev" and "Password" with masked characters ".....". To the right of the password field is a link "Forgot password?". At the bottom center is a green "Login" button with circular icons on either side. Below the button is the text "Don't have an account?".

Username

carlos_dev

Password

.....

[Forgot password?](#)

Login

[Don't have an account?](#)

https://drive.google.com/file/d/1--TljTwYSLgOMoaZBE_TWBJBCXQLv8-k/view?usp=drive_link



our team



**Pablo
Ferrería Hijón**
CMO + CFO

PILOT USERS

Jesús Villalba
Javier Ruiz
Álvaro Baladrón
Lucía Campos



**Miguel
Prado Jiménez**
CEO



**Pablo
Romero Gómez**
CPO

EVENTS & CALENDARS


Jose Manuel Moreno
Manuel Alcaraz
Alberto Valenzuela
Luis Gómez de Terreros
Rafael Pineda
Mario Rivas



**Aarón Jesús
Acuña Bellido**
CTO

INFRA & QA

Raúl Calero
Álvaro Barragán
Diego Manzanos
Alba González
Javier Arellano



**Salvador Ramón
Espinosa Merino**
COO

PROFILE & UX

Antonio Roldán
Alejandro Parody

**+NO
CODE**



teambuilding



After-class meetups

Building trust

Better synergy




Proven useful! ✓



our work methodology

Sprint Planning



Weekly Planning



Weekly Review



Weekly Retro




our work methodology



Feedback



Retrospective



Planning



our work methodology



PERT Estimation



Complexity Weight



Individual Pacing

Backlog

Todo

In Progress


Quality Assurance

Done

Father issues



CI/CD workflows

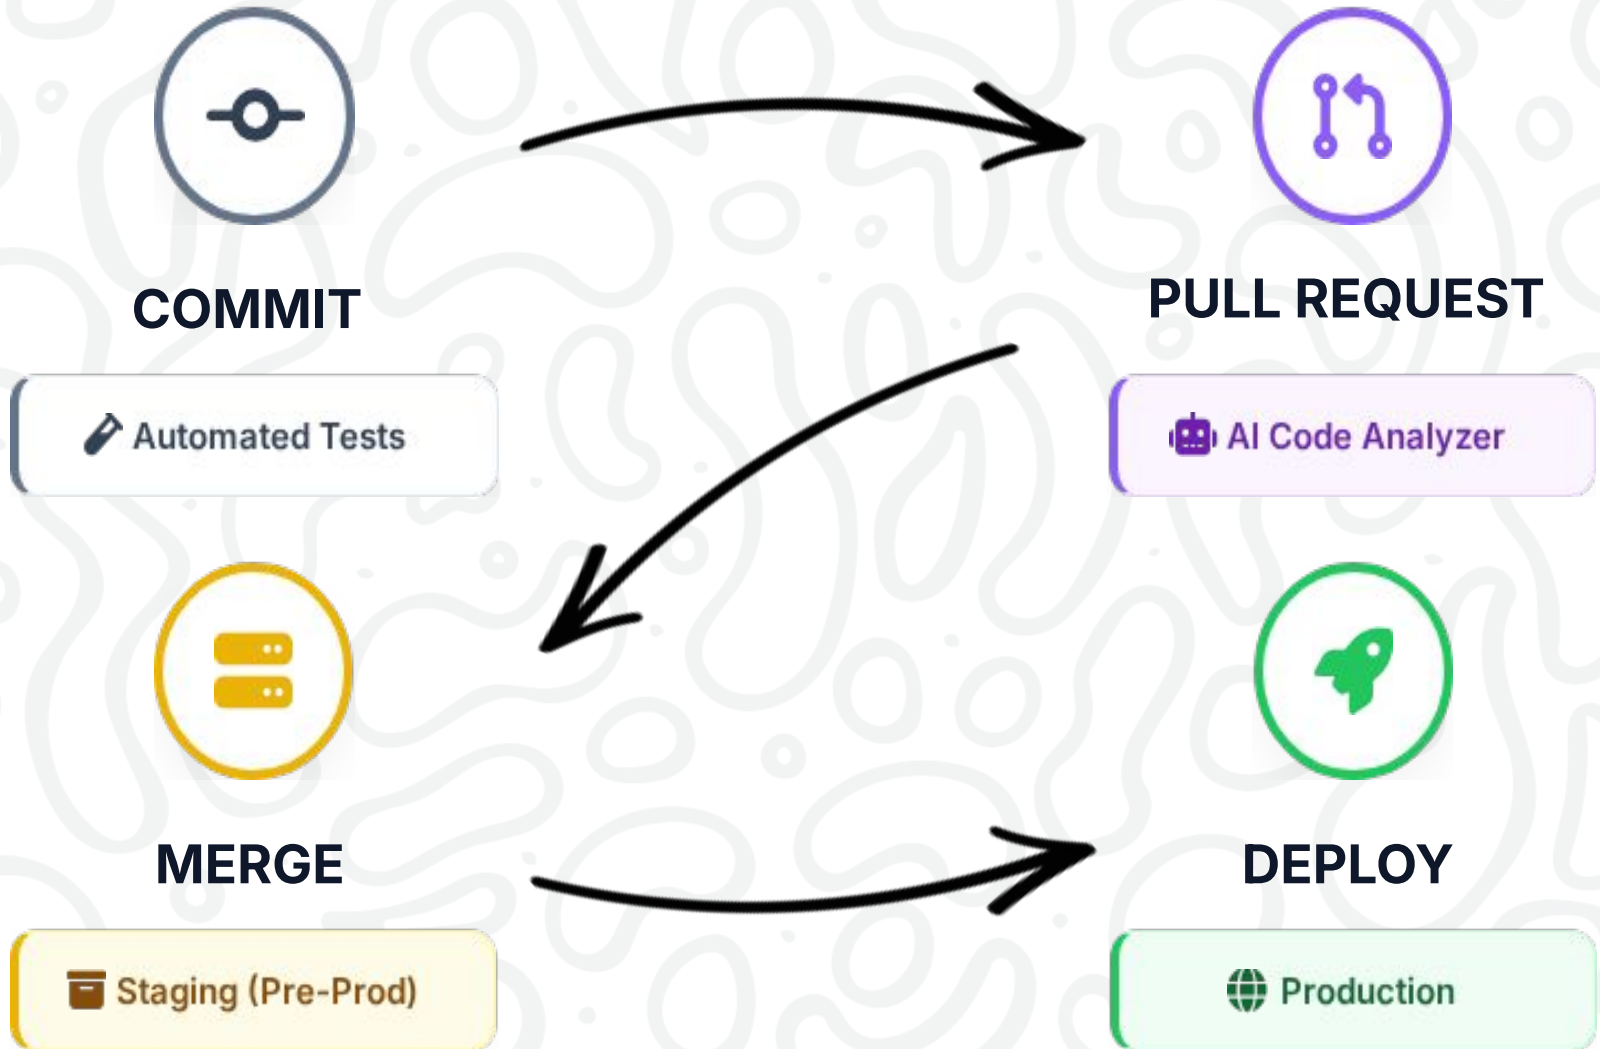


application lifecycle management

pre-commit



continuous integration





sonarqube

continuous deployment



monitoring and feedback




tech stack

DEVELOPMENT



PREPRODUCTION

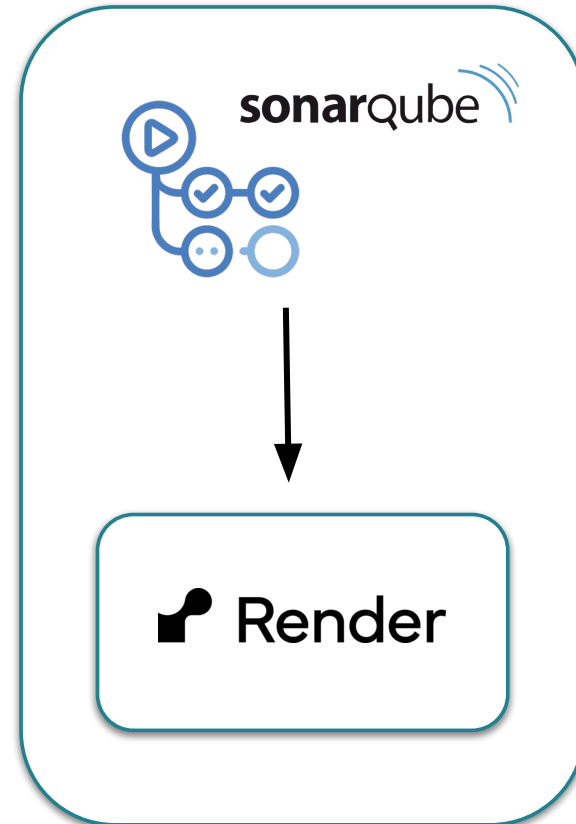


tech stack

PRODUCTION




...



TEAM TOOLS



Communities



testing

what do we currently ;) have ?



Integration test + Unit test = 335 total

70% ⇒ 81% coverage

coverage metrics

Coverage

75% minimum in backend

Objectives for specific modules



Predefined test cases for:

**Integration
E2E**



Module	Planned	Actual	Success?
Reports	85%	100%	✓
Notifications	80%	98%	✓
Events	85%	97%	✓
Radar	70%	97%	✓
Users	90%	96%	✓
Comments	75%	94%	✓
Auth	80%	89%	✓
Calendars	75%	66%	✗
Utils	70%	60%	✗
TOTAL	75%	81%	✓



tools by tests type

Type of test	Tool
Unit	Django TestCase / APITestCase
Integration	Django APITestCase + GraphQLTestCase
E2E	Manual (pre-production)
Acceptance	Manual (pre-production)
Exploratory	Manual (pre-production)
Load / Stress	Locust
Coverage	coverage.py → SonarQube



used tools

SonarQube

Quality, CI/CD

GitHub Actions



sprint 2 retrospective

**WE KEEP IMPROVING
SPRINT BY SPRINT**



**however, there is always some
room for improvement...**



sprint 2 retrospective: things we did well

ACTION

Frontend &
Backend teams



Feature based
organisation

ACHIEVEMENTS

- Faster task completion

- Better communication within modules



MEASUREMENT

Average time
between backend
and frontend
completion



SPRINT 1 RESULT:

16.4h - 1.0d
F - B

SPRINT 2 RESULT:

2.6d - 1.0d
F - B



sprint 2 retrospective: things we did well

ACTION

Set Internal
deadlines for
mid-sprint
deliverables



ACHIEVEMENTS

- Decrease in PR bottlenecks
- Higher morale generally speaking
- Earlier visible results

MEASUREMENT

Average time
from PR creation
until merging



SPRINT 1 RESULT:

1.6d

SPRINT 2 RESULT:

22h



sprint 2 retrospective: problems faced

PROBLEM

Technical Debt
Accumulation



SOLUTION

- Mandatory test implementation
- Re-usability of components and backend utils
- Code maintainability tasks

MEASUREMENT

$$\frac{\text{Refactoring time}}{\text{Development time}}$$

THRESHOLD:

10 - 15%

SPRINT 2 RESULT:

26%


We'll revisit it next week



sprint 2 retrospective: problems faced

PROBLEM

Late task assignment



SOLUTION

- Rough task assignment for whole sprint at the beginning

MEASUREMENT

Correctly assigned tasks
at the beginning

Total # of tasks

THRESHOLD:

85 % accuracy

SPRINT 2 RESULT:

N/A

We'll revisit it in 2 weeks



current status of issue tracking

ISSUE	METRIC	GOALS	STATUS
Poor estimation of time and resources	Complexity standard deviation	<1	0,9524
Lack of communication between coordinators	Number of issues	<3	5
Team members who do not work	Individual effort metric	<4	1
Pull request bottlenecks	Review time	<4	33
Technical debt accumulation	Refactoring tasks per week	>= 1	4



commitment agreement



TEAM

Leaders Defined

Clear reporting

Teams based on modules



MINDSET

Max Grade Goal

Fixed scope

Clear idea



commitment agreement



TIME & TOOLS

10h/Week Mandatory

Tracked in Clockify

More than 7h/week for
safe work



CONFLICTS



Asymmetric Grading

Voluntary Exit

Justify absences/delays



how are we keeping up? (sprint 2)

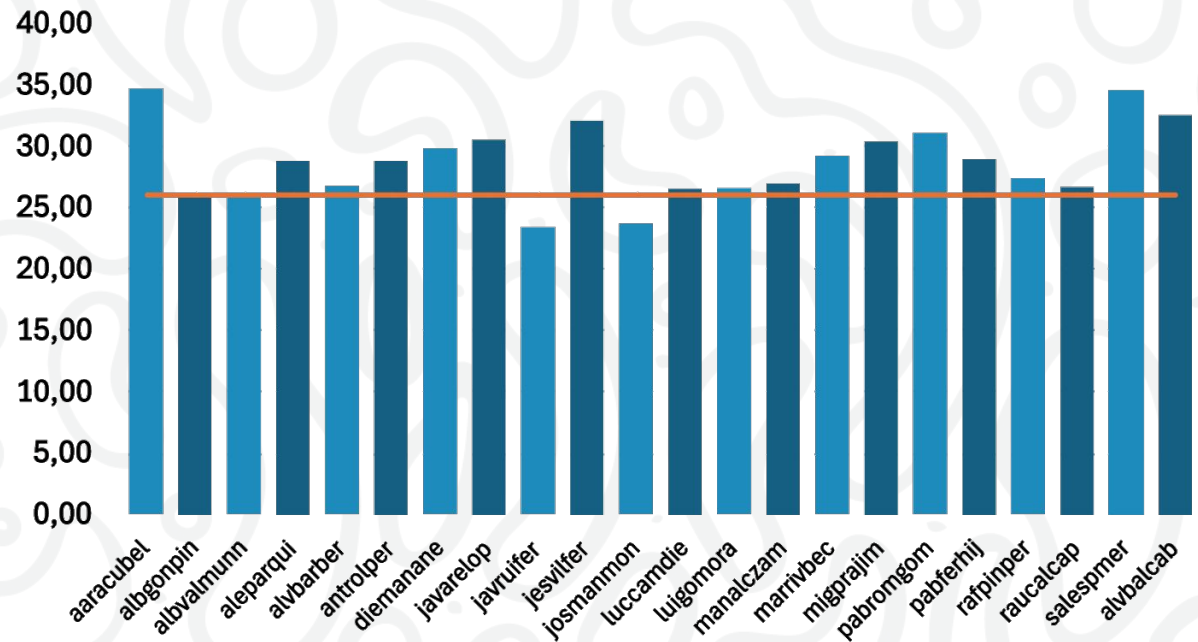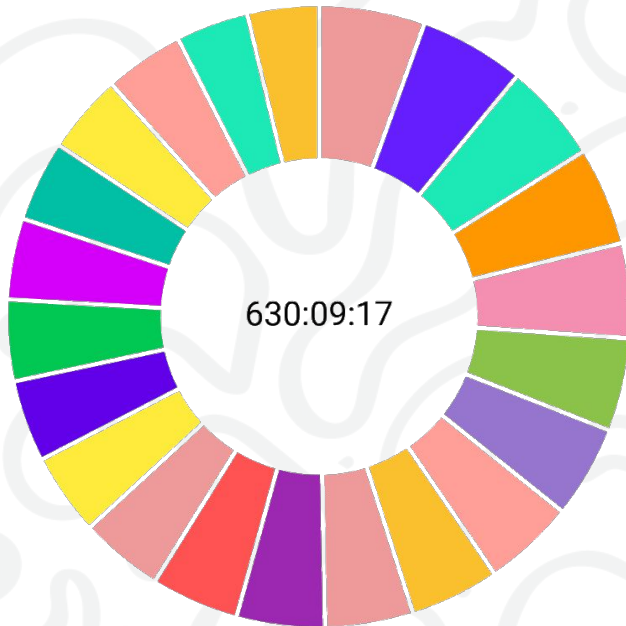



**21
22** team members
over 90%
(23.4h)



mean: 28.64h
median: 28.76h
Std Dev: 3.07h



how are we keeping up? (total)

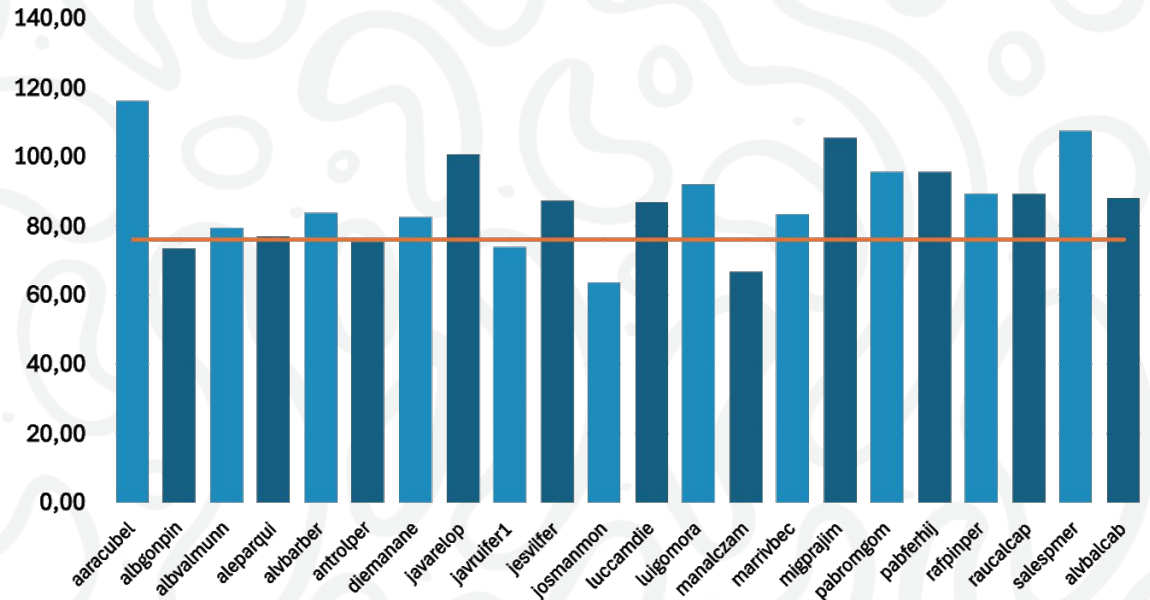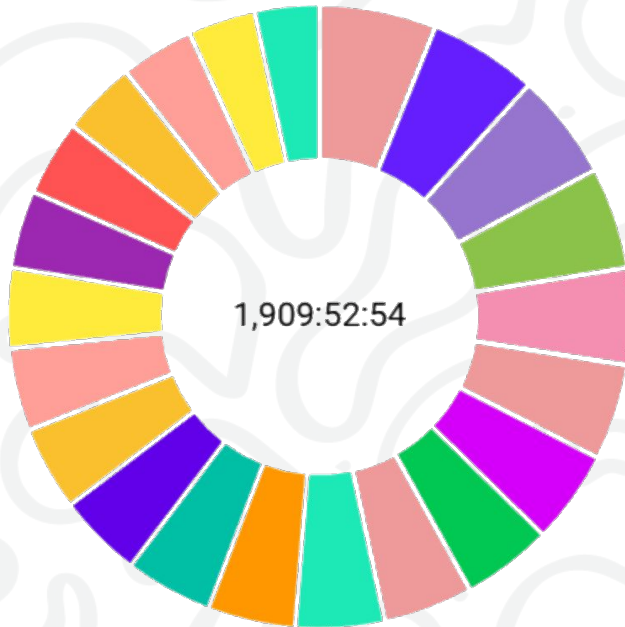

**20
22** team members
over 90%
(68.4h)



mean: 86.81h
median: 86.79h
Std Dev: 13.17h



how do we measure performance in the team?

Complexity of a task * hours/4



Developer

Complexity of a task + Features developed/5 - Solicited changes/5 - Overdue days - Task no moved in kanban/20



Organizer

Pr's reviewed/10 - Pr's reviewed wrong/5 - Overdue days on Pr's/5




QA

Task supervised/20 - Overdue days on supervised tasks without notifying/4




how do we measure performance in the team?


Hours x Accumulated complexity Scatter Plot

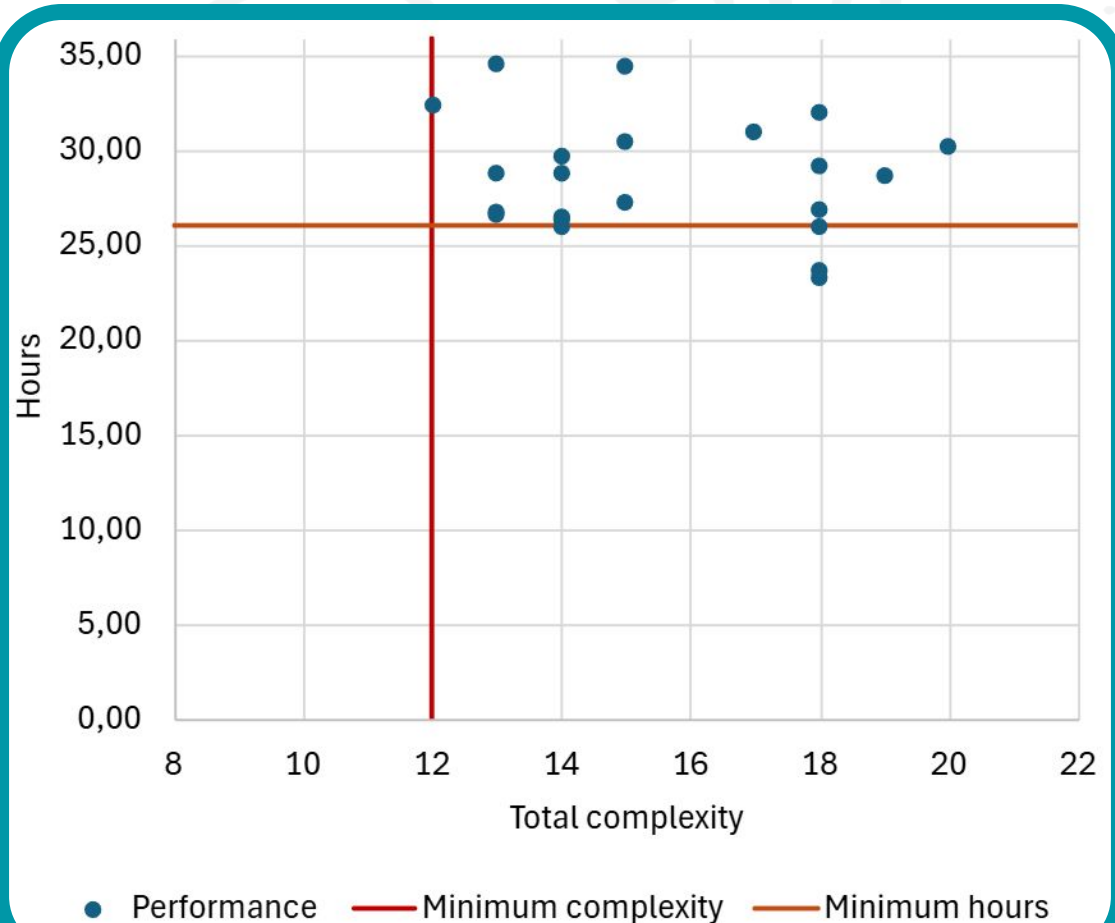


sprint 2 progress

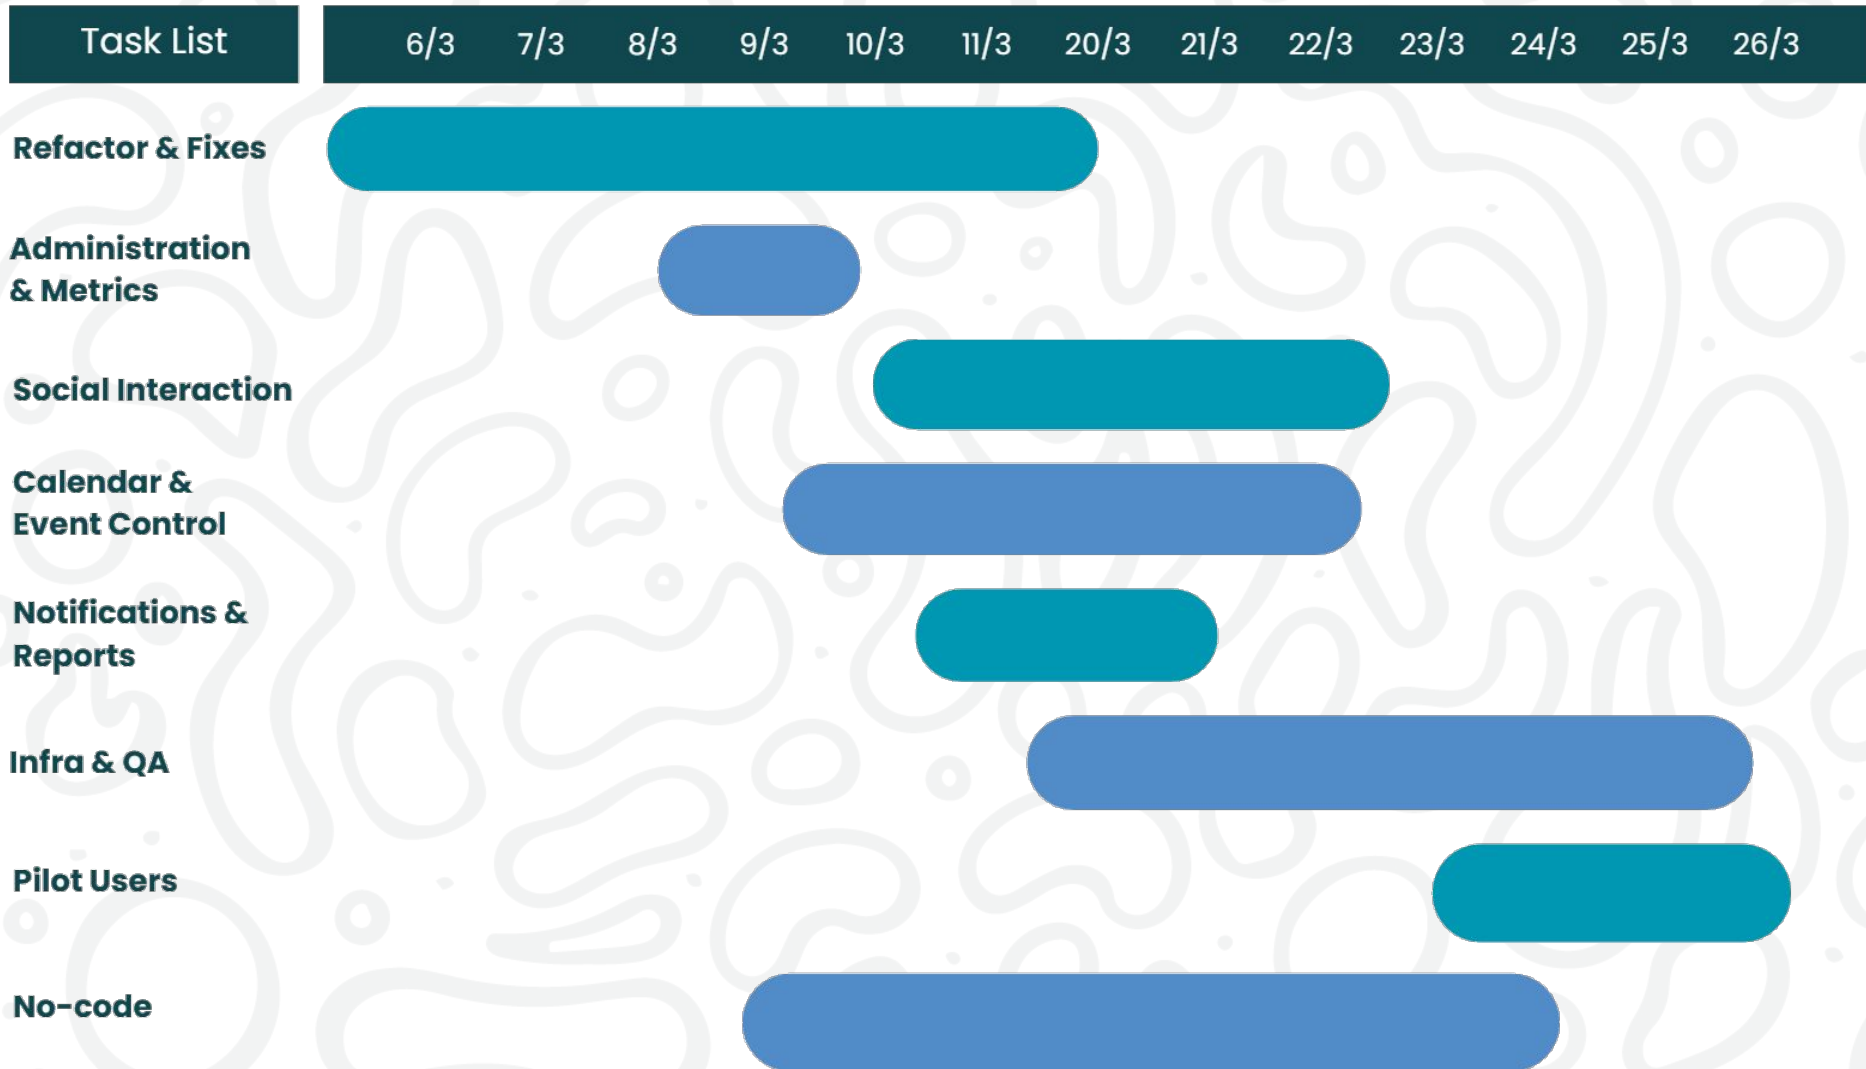


looking forward to sprint 3

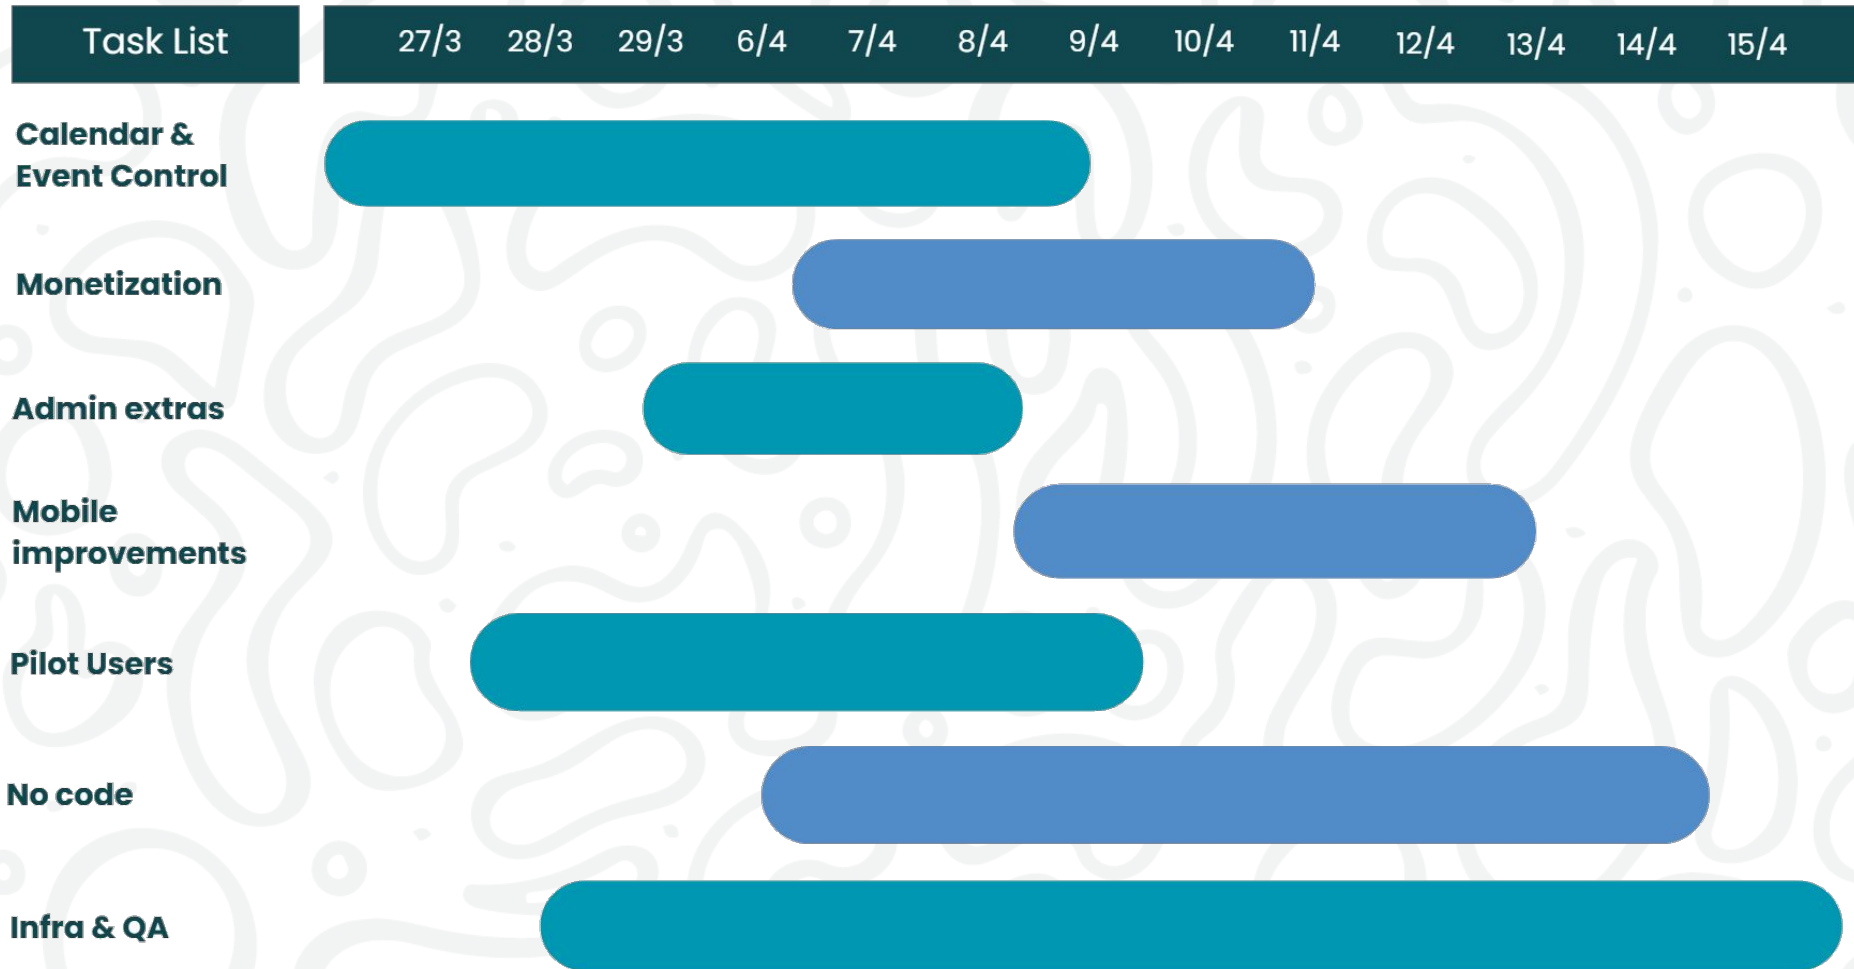

sprint 3 in detail

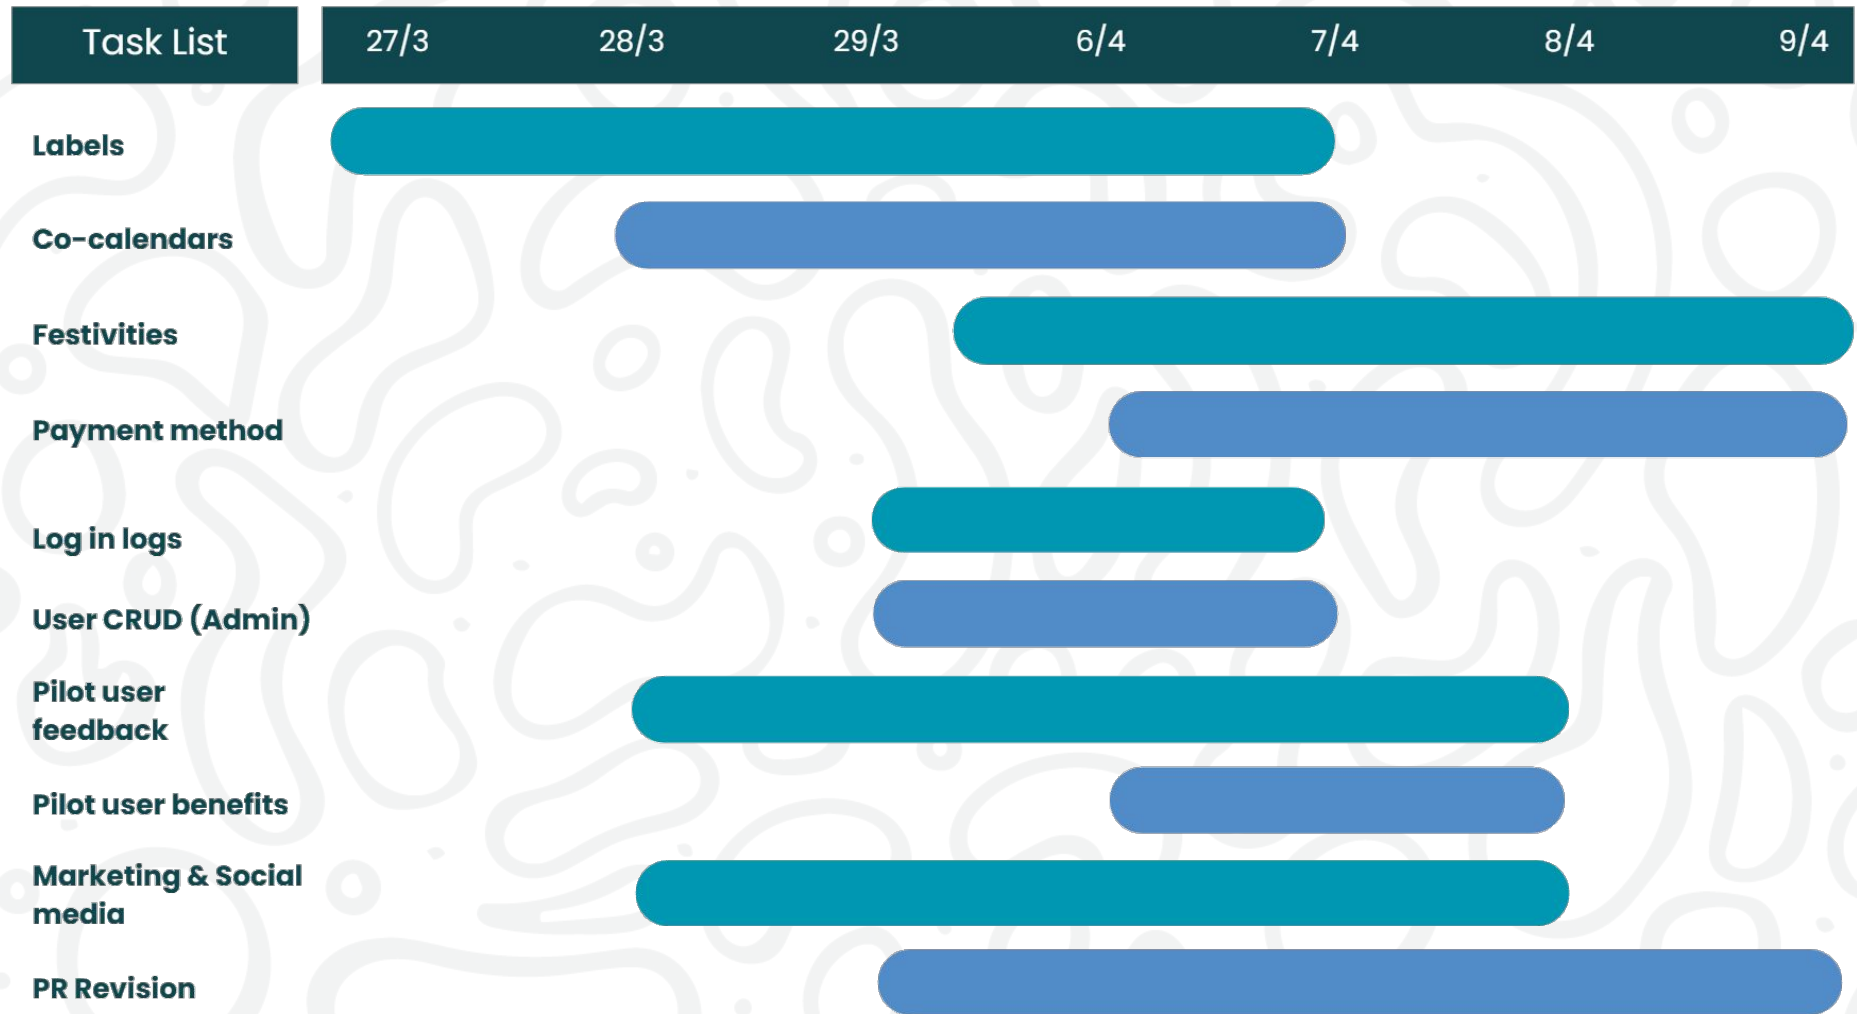

sprint 3 in detail

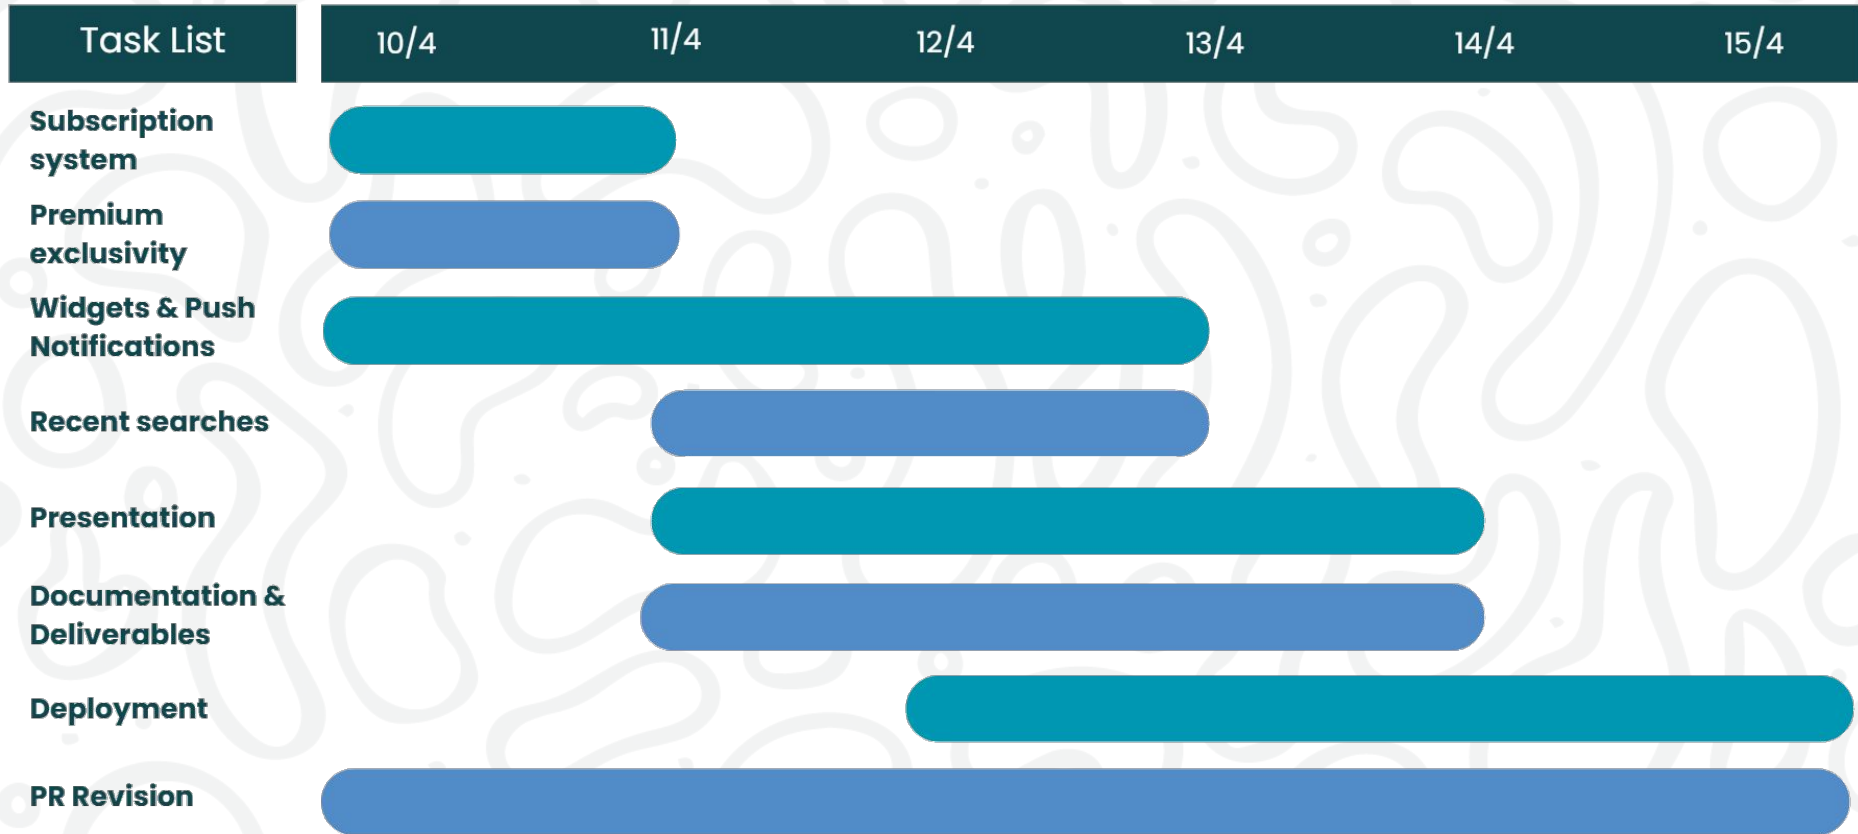

the state of the market



what makes us stronger

	Calendar focused	Follower model	Discovery Tab	Location features	Reward system	Productivity features
current	✓	✓	✓	✓	✓	✓
Eventbrite	✗	✓	✓	✓	✗	✗
Luma	✗	✗	✓	✓	✗	✗
Partiful	✗	✓	✓	✓	✓	✗
Bitrix24	✓	✗	✗	✗	✗	✓
Google Calendar	✓	✗	✗	✓	✗	✗



pilot users update


67
PILOT USERS

list of users


A.C. H	M. C.	L.G.C	G.C.C
F. G	D. W.	L.M.S	G.E.R
I. F. G	C. G. L.	S.P	F.P.J
S. G. C	P. Q. Y	G.M.S	M.M.
P. E. L	P. F. S	J.M.M	P.M.T
M. B	A. S. B	J.G.D	F.M.
A. M. G	A. B. R	P.M.H	G.B.S
A. G	M. F.	S.P.C	A.A.L
N. A. L	V. V. F	A.P.S	R.L.M
P. M. S	A. B. C	S.P.C	F.P.G
E. G. S	J. G. G	A.J.O	R.A.R
P. R. L	I. J. Z	C.P.P	J.A.
A. G. C	M. R. V	V.B.S	S.R.R
M. D. B	J. S. P	A.R	A.P.
A. P. B	C. V. H	B.R.F	L.I.B
S	J. B.	J. G. P.	J. A. D. B.
D. A. L	N. J. S.	R/P9	



pilot users way of contact

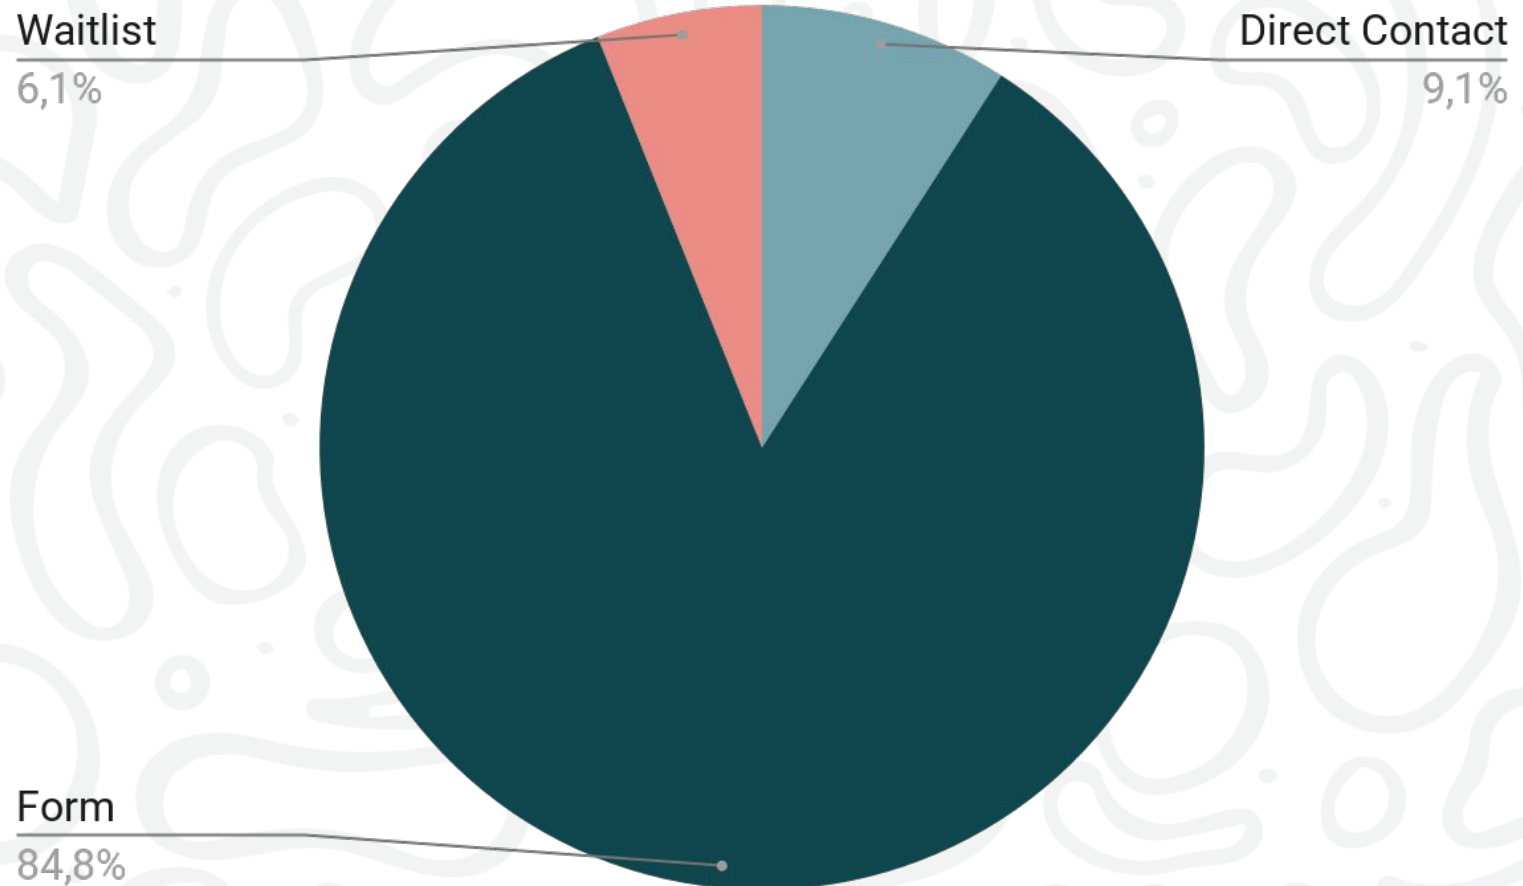


pilot users user profile

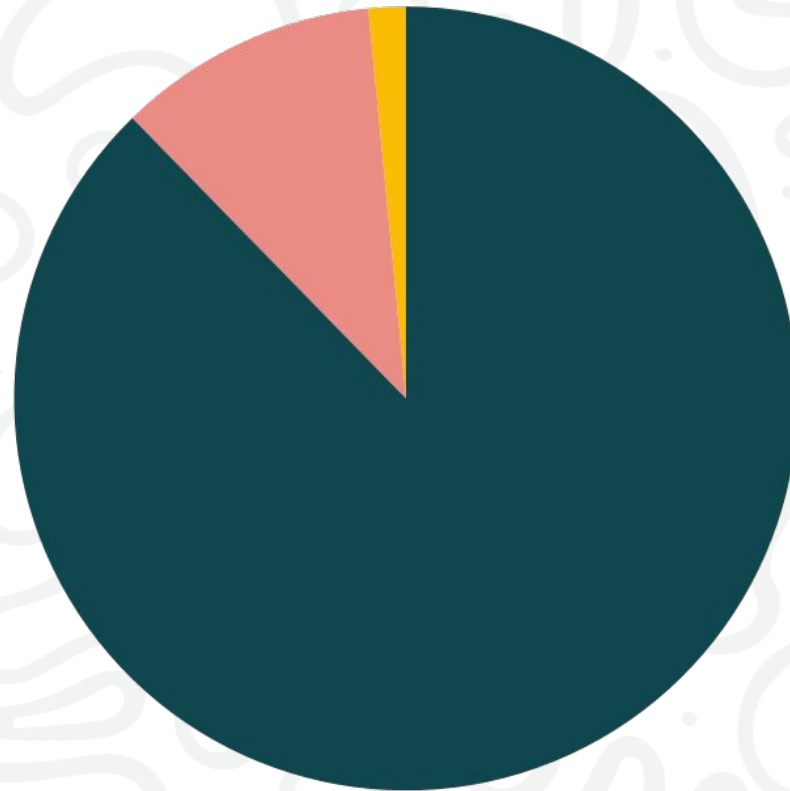


● Event Assistant ● Community Manager ● Empresa



pilot users feedback management

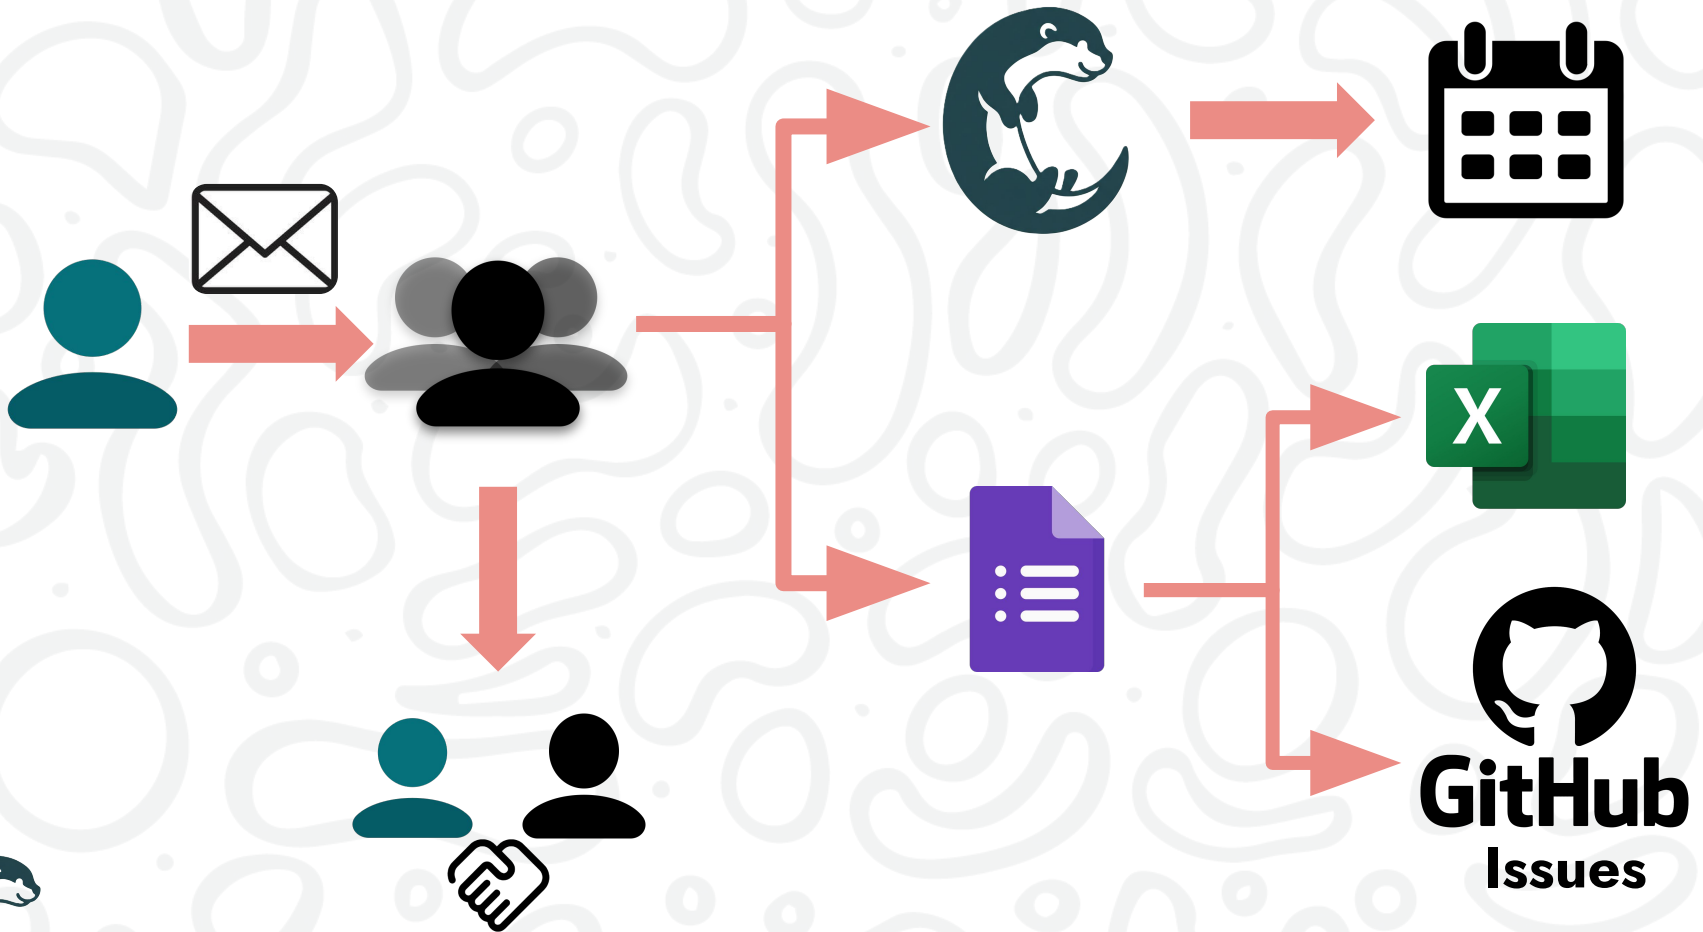

pilot users feedback management

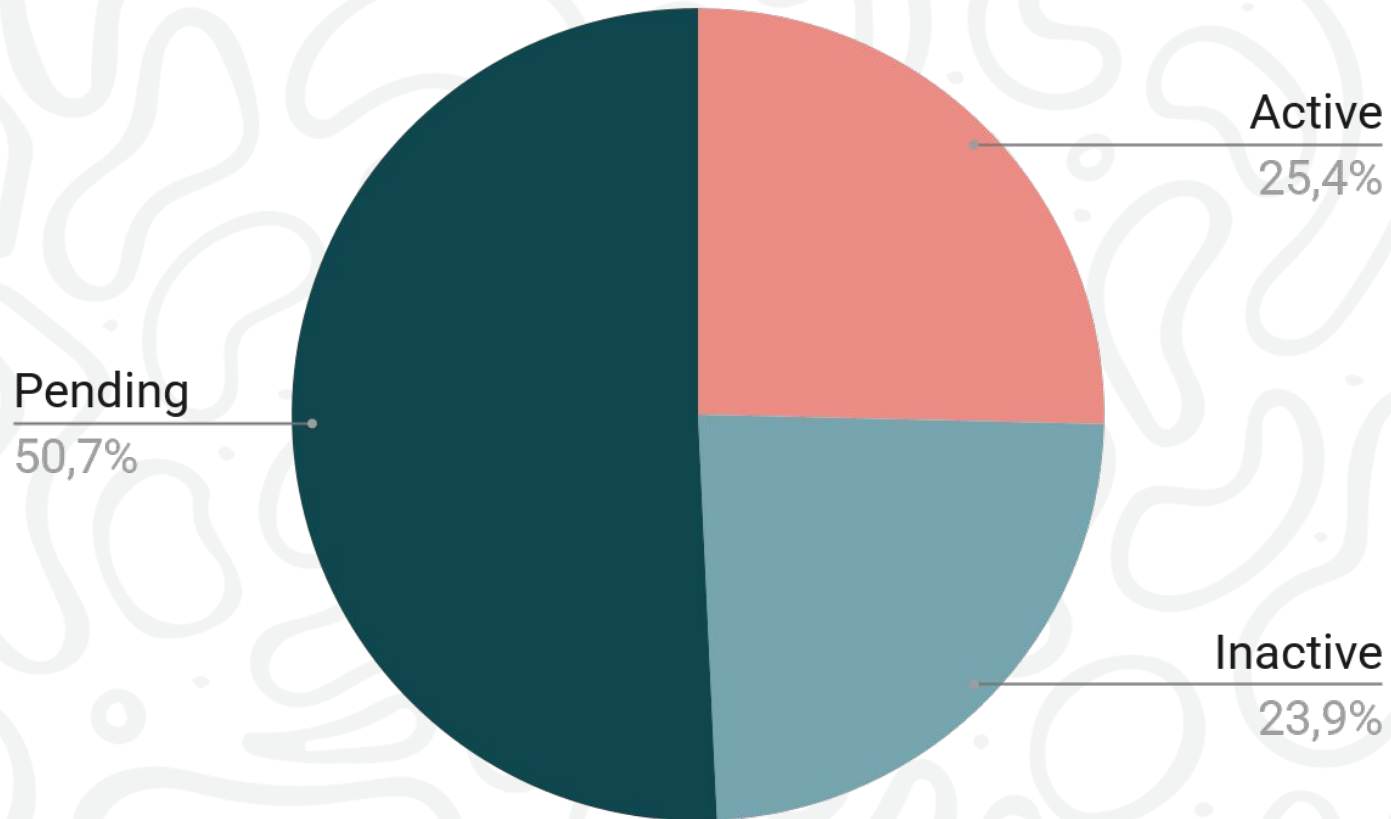

pilot users **social media campaigns**



engagement strategies



"Ready to use" Calendars

Exam days, LaLiga matches... All preloaded and ready to share with a link



"Phygital" Integration

QR codes in bars, cafes, universities... showing the digital agenda of that place with offers or events



Mail Reminders and Updates

Updating any inactive or pending users to fulfill their feedback forms and use the app



economical analysis

Role	People	Hours	Gross Cost	Social Security (31,4%)	Total Cost
Frontend Designer	6	360h	6.480,00 €	2.034,72 €	8.514,72 €
Backend Engineer	7	490h	8.820,00 €	2.769,48 €	11.589,48 €
Cybersecurity	2	40h	760,00 €	238,64 €	998,64 €
DevOps / QA	2	40h	760,00 €	238,64 €	998,64 €
Management	5	15h	315,00 €	98,91 €	413,91 €
TOTAL	22	945h	17.135,00 €	5.380,39 €	22.515,39 €



year 1 - cost summary

Concept	Monthly Cost	Annual Cost
Databases (Pre y Pro)	7,20 \$/month	86,40 \$/year
Storages (DigitalOcean Spaces 250 GB)	5,00 \$/month	60,00 \$/year
Load Balancer	12,00 \$/month	144,00 \$/year
Kubernetes	12,00 \$/month	144,00 \$/year
TOTAL (EUR aprox.)	~30,66 €/month	367,94 €/year



CAPEX

Ltd. Constitution:

400 €




OPEX

Concepto	Importe Anual
Development	23.677,29 €
No-code tasks	3.880,93 €
Owner Manager (CEO) — Full rate - year 1	1.020,00 €
Tax and workforce management	1.800,00 €
Cloud (Digital Ocean) Infrastructure	367,94 €
Domain (.com)	8,46 €
Additional storage	10,00 €
Social media campaigns (TikTok/Reels/Instagram)	600,00 €
YEARLY OPEX COSTS	31.364,62 €
Monthly operating cost (survival)	~2.613,72 €/month




accumulated **cost** VS accumulated **revenue**

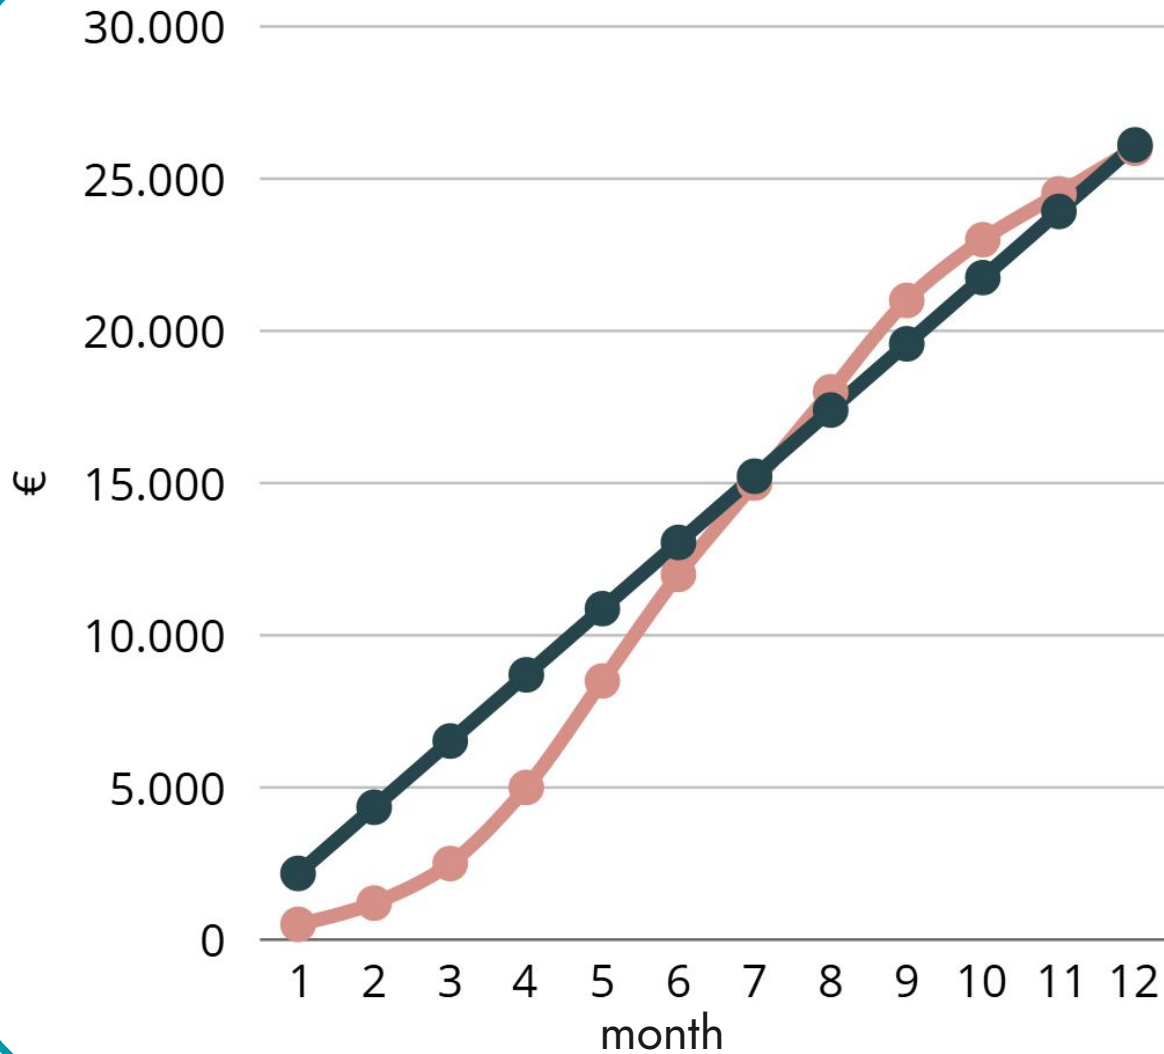

equilibrium point

- **Business earnings**
- **Standard earnings**
- **Costs**

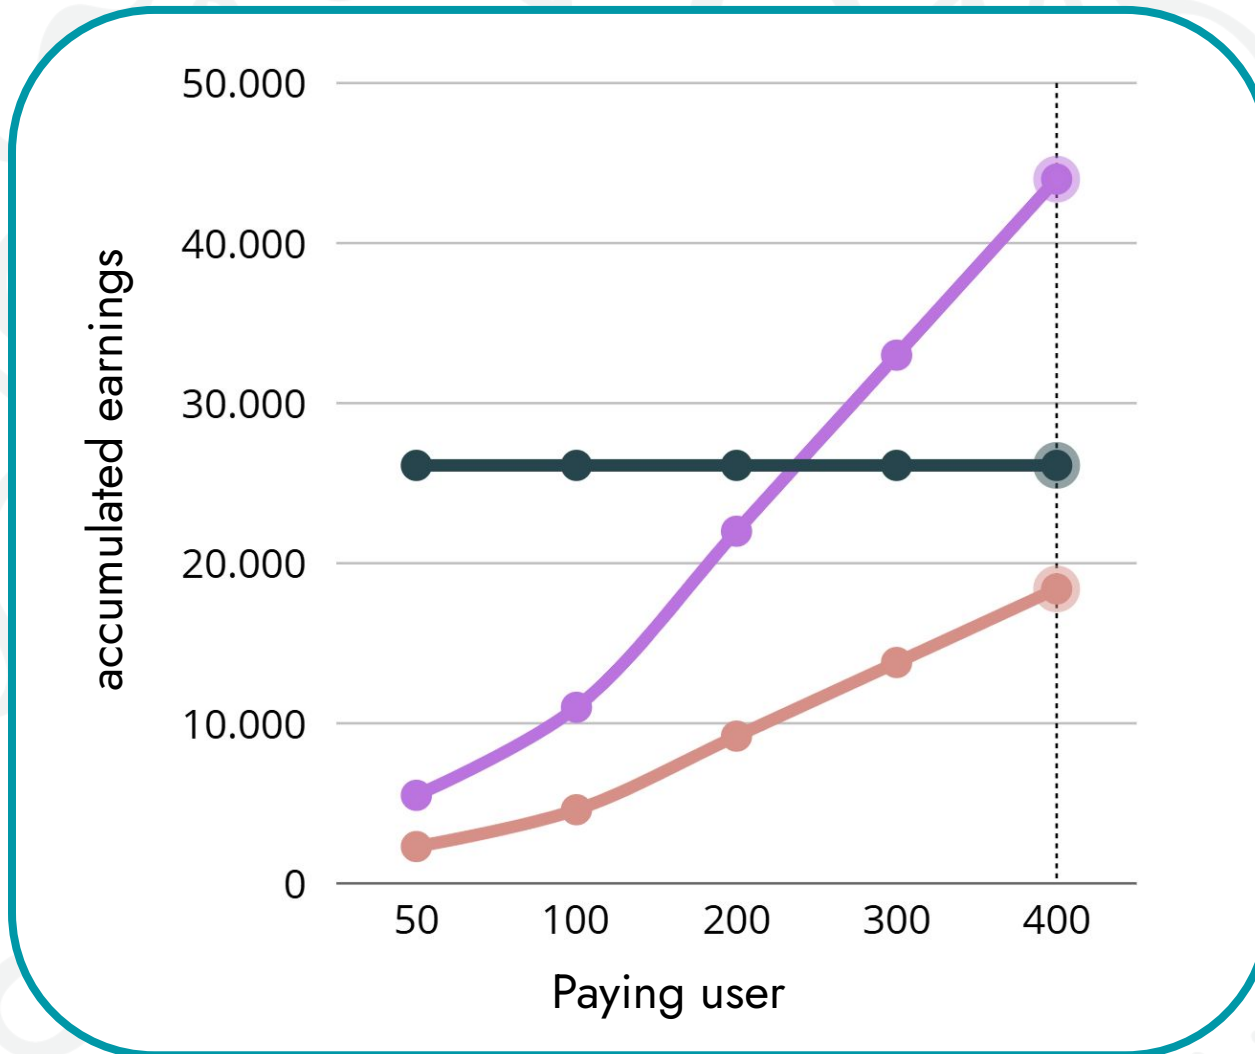

monetization by freemium model

FREE PLAN

All core functions, but limited

Some limitations:

- Unlimited interactions
- 10 favorites calendars max.
- 2 public calendars
- 2 private calendars
- Media and Personalisation Limitations
- Map shows only same day events

INCLUDES ADS



our premium packs

STANDARD PACK

4.99€/monthly

Ideal for users seeking a complete experience

All of Free Plan plus:

- Unlimited calendars
- Unlimited favorites
- Verified Badge
- Calendar Personalisation
- Full Media additions
- Full Map Access

ANNUAL STANDARD PACK

45.99€ ~~59.99€~~



our premium packs

BUSINESS PACK

9.99€/monthly

Ideal for influencers and companies that want to grow

All of Standard Pack plus:

- Calendar analytics
- Promote calendars
- Verified Badge
- Chat for event goers
- Business/Creator Badge

ANNUAL BUSINESS PACK

109.99€ ~~119.99€~~





our socials



our landing page



check it out yourselves!

Questions?
Feedback?

**TIME TO
ASK!**

